ED REDEVELOPMENT
CROYDON UNIVERSITY HOSPITAL
PROGRAMME OVERVIEW

Fri 14/02/14

ID	Task Name	Start	Finish
1	**OBC PROCESS**	**Fri 28/02/14**	**Fri 25/04/14**
2	Issue OBC Checklist	Fri 28/02/14	Fri 28/02/14
3	OBC Approval Process	Mon 03/03/14	Fri 25/04/14
4	**PLANNING PROCESS**	**Mon 17/02/14**	**Wed 02/07/14**
5	**Decant Works**	**Mon 17/02/14**	**Fri 13/06/14**
6	Prepare Drawings/ Documents	Mon 17/02/14	Fri 07/03/14
7	Documents/ Drawings Approval by Trust	Mon 10/03/14	Fri 14/03/14
8	Issue Planning	Mon 17/03/14	Mon 17/03/14
9	Determination Period	Mon 17/03/14	Fri 13/06/14
10	**Main Works**	**Mon 17/02/14**	**Wed 02/07/14**
11	Prepare Drawings/ Documents	Mon 17/02/14	Tue 25/03/14
12	Documents/ Drawings Approval by Trust	Wed 26/03/14	Wed 02/04/14
13	Issue Planning	Thu 03/04/14	Thu 03/04/14
14	Determination Period	Thu 03/04/14	Wed 02/07/14
15	**STAGE 3**	**Mon 03/02/14**	**Fri 13/06/14**
16	Surveys	Mon 03/02/14	Fri 28/02/14
17	Detailed Design Information	Mon 17/02/14	Fri 13/06/14
18	**GMP**	**Tue 27/05/14**	**Wed 06/08/14**
19	BQ Production and Tender Process	Tue 27/05/14	Tue 05/08/14
20	Issue GMP	Wed 06/08/14	Wed 06/08/14
21	**FBC PROCESS AND CONTRACT**	**Mon 23/06/14**	**Tue 21/10/14**
22	Trust Prepare FBC	Mon 23/06/14	Tue 19/08/14
23	Submit FBC to TDA	Wed 20/08/14	Wed 20/08/14
24	TDA Approval Process	Thu 21/08/14	Tue 14/10/14
25	Prepare Contract Documents	Wed 03/09/14	Tue 14/10/14
26	Sign Contract with PSPC	Wed 15/10/14	Tue 21/10/14
27	**DECANT WORKS**	**Tue 08/04/14**	**Mon 08/09/14**
28	Kenley 1 Vacated to Dementia	Mon 14/07/14	Mon 14/07/14
29	Kenley 1 Works	Tue 15/07/14	Mon 11/08/14
30	Kenley 2 Works	Tue 08/04/14	Mon 02/06/14
31	Norwood Works	Mon 16/06/14	Fri 11/07/14
32	Temporary Building for UCC (with lead-in)	Mon 16/06/14	Mon 08/09/14
33	Temporary Building to extend Majors	Mon 16/06/14	Mon 08/09/14
34	Temporary Building to extend Paeds	Mon 16/06/14	Mon 08/09/14
35	**MAIN BUILD CONSTRUCTION WORKS**	**Wed 22/10/14**	**Mon 21/12/15**
36	Construction Works inc Mobilisation	Wed 22/10/14	Fri 18/12/15
37	Areas available for occupation	Mon 21/12/15	Mon 21/12/15

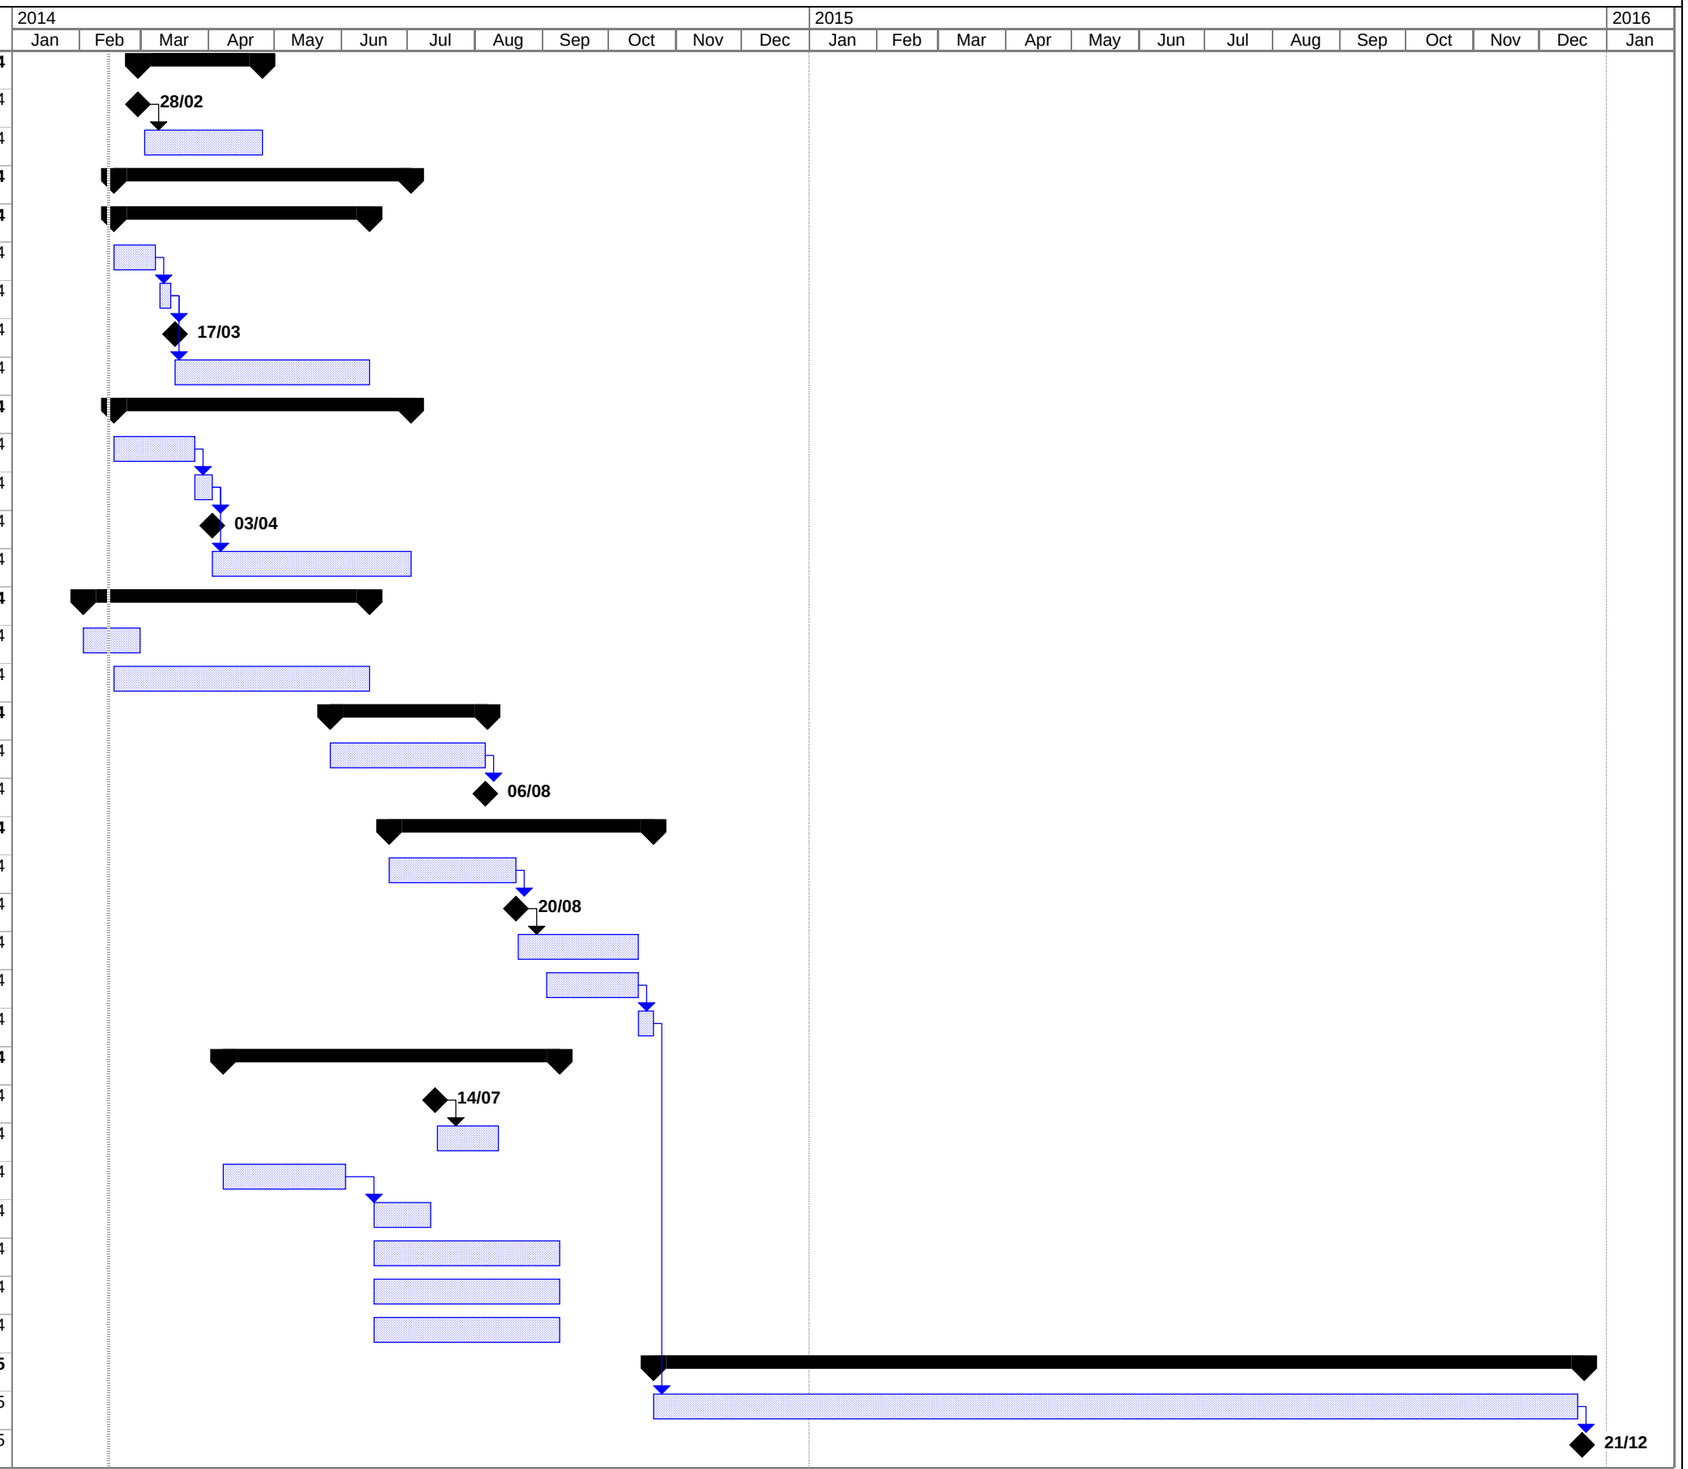

Project: 140214 ED Redevelopment H
Date: Fri 14/02/14

Task | Progress | Summary | External Tasks | Deadline
Split | Milestone | Project Summary | External Milestone
